



HYDROTEST COMPLETION CERTIFICATE



Project: 1 1/4" 1.2 MTRS LENGTH HYDRO TESTING

Piping Detail: EUROTHERM PPR PN 20 FULL BLACK UV PIPE 40MM SIZE PIPE SPOOL WITH REDUCER FITTING SOCKET / FEMALE THREAD

Date	2nd Feb, 2025
Location	MISFAH YARD-OMAN
Hydro Test Pressure (Bar)	37.5
Client/Contractor	Eutotech
Test Pack Number	01

Piping Spool Size (inch)	1 1/4 "
Piping Spool Length (Mtrs)	1.2
Volume(Ltrs)	0.6
GPS PO No / Work Order No	Arshad Ahamed-Eurotech International LLC / Mail Reference

This is to certify that

EUROTHERM PPR PN 20 FULL BLACK UV PIPE 40MM SIZE PIPE SPOOL WITH REDUCER FITTING SOCKET / FEMALE THREAD ADAPTER 40mmX32MM

Piping Spool

Was successfully hydrotested by **GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC** Representative

HYDROTEST PARAMETER'S

LOCATION OF TEST	MISFAH GPS YARD					
TEST MEDIUM	WATER					
AIR CONTENT % OF PIPELINE @ 50% OF TP	N/A					
VISUAL INSPECTION @ 100% OF TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.5	FINAL PRESSURE	37.5
STRENGTH TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.5	FINAL PRESSURE	37.5
LEAK TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	MAX PRESSURE	37.5	MIN PRESSURE	37.5
ACTUAL CHANGE IN TEMPERATURE AT TEST PRESSURE (DEG C)						N/A °C
ALLOWABLE CHANGE IN PRESSURE AT TEST PRESSURE						N/A Barg
ACTUAL CHANGE IN PRESSURE AT TEST PRESSURE						N/A Barg
DURATION OF PRESSURISATION	30 Mins	FROM: 2nd Feb, 2025 14:30 Hrs	TO: 2nd Feb, 2025 15:00 Hrs			
DURATION OF STRENGTH TEST	1 Hour	FROM: 2nd Feb, 2025 15:00 Hrs	TO: 2nd Feb, 2025 16:00 Hrs			
DURATION OF LEAK TEST	1 Hours	FROM: 2nd Feb, 2025 15:00 Hrs	TO: 2nd Feb, 2025 16:00 Hrs			

INSTRUMENT'S DETAILS

INSTRUMENT DESCRIPTION	INS SERIAL NO	RANGE	CALIBRATION DATE	CALIBRATION DUE DATE
PRESSURE RECORDER	112160072004	0-60 Bar	17 Nov 2024	16 Nov 2025
PRESSURE GAUGE	90018DM9	0-60 Bar	17 Nov 2024	16 Nov 2025
PRESSURE GAUGE	90018DM1	0-60 Bar	17 Nov 2024	16 Nov 2025
PRESSURE SAFETY VALVE	908559	45 Bar	24th Aug, 2023	23rd Aug, 2024

Comments:

EUROTHERM PPR PN 20 FULL BLACK UV PIPE 40MM SIZE PIPE SPOOL WITH REDUCER FITTING SOCKET / FEMALE THREAD ADAPTER 40mmX32MM HYDRO TESTING COMPLETED SUCCESSFULLY AT A PRESSURE OF 37.5 BARG

Completed By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	SHREE RAM YADAV	Signature:	Date: 2nd Feb, 2025
Designation:	TESTING SUPERVISOR		

Approved By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	PARTHIBAN	Signature:	Date: 2nd Feb, 2025
Designation:	TESTING ENGINEER		



MODERN PROJECTS AL GHUBRA LLC

GPS Doc Reference No:

GPS-ET-2025-01

Page No

1 OF 1

13 14 15 16 17 18

EUROTECH PNR PR 20 FULL BLACK UV PIPE 40MM SIZE
 FITTING WITH PN 25 REDUCER SOCKET 40x32MM UV IN BOTH END

100% OF DIP
 75% OF DIP
 50% OF DIP
 25% OF DIP

1HR HOLDING PERIOD
 DEPRESSURISING STARTED

ON
 METER NO.
 DISC NO.
 OFF
 LOCATION
 M
 M
 REMARKS
 BUKC-2128

GLOBAL PIPELINES SERVICES	
PROJECT NAME	1 1/2" & 3" UV PIPE 1.2M LENGTH HYDRO TEST
CLIENT / LOCATION	EUROTECH / MUSCAT
ACTIVITY	HYDRO TEST
TEST PACK NO/NAME	PP-02 / 40MM SIZE PIPE SPOOL (1 1/4" PIPE SPOOL) WITH REDUCER FITTING
CHART ON DATE/TIME	02/02/2025 / 14.30 HRS
CHART OFF DATE/TIME	02/02/2025 / 16.15 HRS
PRESSURE REC./GAUGE NO	112160072004 / 90018D9 90018D1



HYDROTEST COMPLETION CERTIFICATE



Project	3" 1.2 MTRS LENGTH HYDRO TESTING
Piping Detail	EUROTHERM PPR PN 20 FULL BLACK UV PIPE 90MM SIZE PIPE SPOOL WITH REDUCER FITTING SOCKET / FEMALE THREAD

Date	2nd Feb, 2025
Location	MISFAH YARD-OMAN
Hydro Test Pressure (Bar)	37.5
Client/Contractor	Eurotech
Test Pack Number	02

Piping Spool Size (inch)	3"
Piping Spool Length (Mtrs)	1.2
Volume(Ltrs)	5.4
GPS PO No / Work Order No	Arshad Ahamed-Eurotech International LLC / Mail Reference

This is to certify that **EUROTHERM PPR PN 20 FULL BLACK UV PIPE 90MM SIZE PIPE SPOOL WITH REDUCER FITTING SOCKET / FEMALE THREAD ADAPTER 90mmX63MM** Piping Spool

Was successfully hydrotested by **GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC** Representative

HYDROTEST PARAMETER'S

LOCATION OF TEST	MISFAH GPS YARD					
TEST MEDIUM	WATER					
AIR CONTENT % OF PIPELINE @ 50% OF TP	N/A					
VISUAL INSPECTION @ 100% OF TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.5	FINAL PRESSURE	37.5
STRENGTH TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.5	FINAL PRESSURE	37.5
LEAK TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	MAX PRESSURE	37.5	MIN PRESSURE	37.5
ACTUAL CHANGE IN TEMPERATURE AT TEST PRESSURE (DEG C)					N/A	°C
ALLOWABLE CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
ACTUAL CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
DURATION OF PRESSURISATION	25 Mins	FROM: 2nd Feb, 2025	12:30 Hrs	TO: 2nd Feb, 2025	12:55 Hrs	
DURATION OF STRENGTH TEST	1 Hour	FROM: 2nd Feb, 2025	12:55 Hrs	TO: 2nd Feb, 2025	14:00 Hrs	
DURATION OF LEAK TEST	1 Hours	FROM: 2nd Feb, 2025	12:55 Hrs	TO: 2nd Feb, 2025	14:00 Hrs	

INSTRUMENT'S DETAILS

INSTRUMENT DESCRIPTION	INS SERIAL NO	RANGE	CALIBRATION DATE	CALIBRATION DUE DATE
PRESSURE RECORDER	112160072004	0-60 Bar	17th Nov, 2024	16th Nov, 2025
PRESSURE GAUGE	90018DM9	0-60 Bar	17th Nov, 2024	16th Nov, 2025
PRESSURE GAUGE	90018DM1	0-60 Bar	17th Nov, 2024	16th Nov, 2025
PRESSURE SAFETY VALVE	908559	45 Bar	24th Aug, 2024	23rd Aug, 2025

Comments:
EUROTHERM PPR PN 20 FULL BLACK UV PIPE 90MM SIZE PIPE SPOOL WITH REDUCER FITTING SOCKET / FEMALE THREAD ADAPTER 90mmX63MM HYDRO TESTING COMPLETED SUCCESSFULLY AT A PRESSURE OF 37.5 BARG

Completed By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	SHREE RAM YADAV	Signature:		Date:	2nd Feb, 2025
Designation	TESTING SUPERVISOR				

Approved By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

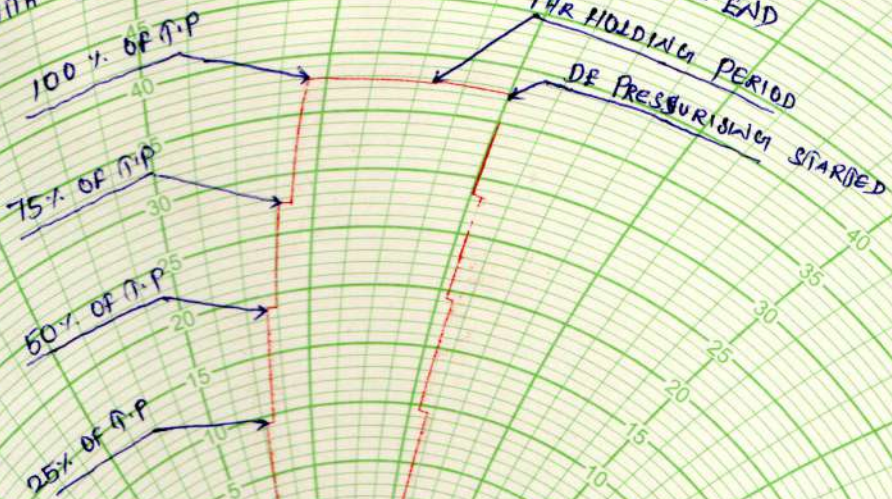
Name:	PARTHIBAN	Signature:		Date:	2nd Feb, 2025
Designation	TESTING ENGINEER				



MODERN PROJECTS AL GHUBRA LLC

GPS Doc Reference No: GPS-ET-2025-02
Page No: 1 OF 1

EUROTHERM PNR PR 20 FULL BLACK UV PIPE 90MM SIZE
 FITTING WITH REDUCER SOCKET 90x60MM UV IN BOTH THE END



BKUC-2128

REMARKS

ON

M

OFF

M




METER NO.

LOCATION

DISC NO.

GLOBAL PIPELINES SERVICES

PROJECT NAME	1 1/4" 33" UV PIPE 1.2M LENGTH HYDRO TEST
CLIENT / LOCATION	EUROTECH / MUSCAT
ACTIVITY	HYDRO TEST
TEST PACK NO/NAME	PP-01 / 90MM SIZE PIPESPOOL (3" PIPE SPOOL) WITH REDUCER FITTINGS
CHART ON DATE/TIME	02/02/2025 / 12:30 HRS
CHART OFF DATE/TIME	02/02/2025 / 14:15 HRS
PRESSURE REC./GAUGE NO	112160072004 / 90018D9 90018DM

	HYDROTEST COMPLETION CERTIFICATE		 <small>PP-R PIPES & FITTINGS</small> 
	Project	2 1/2" 1 MTRS LENGTH HYDRO TESTING	
	Piping Detail	Eurotherm PPR PN25 Pipe 75mm Pipe Spool / Female Thread Adapter75mm to 63mm reducer X of 2 pcs (fitted in both pipe ends)	

Date	15th July, 2024	Piping Spool Size (inch)	2-1/2
Location	MISFAH YARD-OMAN	Piping Spool Length (Mtrs)	2
Hydro Test Pressure (Bar)	37.5	Volume(Ltrs)	3.16
Client/Contractor	EUROTHERM	GPS PO No / Work Order No	Shibili Numan-Eurotech International LLC / Mail Reference
Test Pack Number	04		

This is to certify that Eurotherm PPR PN25 Pipe 75mm Pipe Spool / Female Thread Adapter75mm to 63mm reducer X of 2 pcs (fitted in both pipe ends) **Piping Spool**

Was successfully hydrotested by GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC **Representative**

HYDROTEST PARAMETER'S

LOCATION OF TEST		MISFAH GPS YARD					
TEST MEDIUM		WATER					
AIR CONTENT % OF PIPELINE @ 50% OF TP		N/A					
VISUAL INSPECTION @ 100% OF TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.5	FINAL PRESSURE	37.2	
STRENGTH TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.2	FINAL PRESSURE	37.2	
LEAK TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	MAX PRESSURE	37.2	MIN PRESSURE	37.2	
ACTUAL CHANGE IN TEMPERATURE AT TEST PRESSURE (DEG C)					N/A °C		
ALLOWABLE CHANGE IN PRESSURE AT TEST PRESSURE					N/A Barg		
ACTUAL CHANGE IN PRESSURE AT TEST PRESSURE					N/A Barg		
DURATION OF PRESSURISATION	2 Hour 5 Mins	FROM:	15th July, 2024 13:00	TO:	15th July, 2024 15:05		
DURATION OF STRENGTH TEST	1 Hour	FROM:	15th July, 2024 15:05	TO:	15th July, 2024 16:05		
DURATION OF LEAK TEST	1 Hours	FROM:	15th July, 2024 15:05	TO:	15th July, 2024 16:05		


INSTRUMENT'S DETAILS

INSTRUMENT DESCRIPTION	INS SERIAL NO	RANGE	CALIBRATION DATE	CALIBRATION DUE DATE
PRESSURE RECORDER	11260072004	0-60 Bar	1st Dec, 2023	30th Nov, 2024
PRESSURE GAUGE	9000R81P	0-60 Bar	9th June, 2024	8th June, 2025
DIGITAL PRESSURE GAUGE	707496	0-700 Bar	15th June, 2024	14th June, 2025
PRESSURE SAFETY VALVE	1064356	41 Bar	9th June, 2024	8th June, 2025


Comments:

Eurotherm PPR PN25 Pipe 75mm Pipe Spool / Female Thread Adapter75mm to 63mm reducer X of 2 pcs (fitted in both pipe ends)

Completed By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	VARUN KUMAR	Signature:		Date:	15th July, 2024
Designation	TESTING SUPERVISOR				

Approved By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	SENTHIL KUMAR	Signature:		Date:	15th July, 2024
Designation	TESTING ENGINEER				



HYDROTEST COMPLETION CERTIFICATE



Project	2 1 MTRS LENGTH HYDRO TESTING
Piping Detail	Eurotherm PPR PN25 Pipe 63mm Pipe Spool / Female Thread Adapter 63mm X of 2 pcs (fitted in both pipe ends)

Date	28th June, 2024
Location	MISFAH YARD-OMAN
Hydro Test Pressure (Bar)	37.5
Client/Contractor	EUROTHERM
Test Pack Number	03

Piping Spool Size (inch)	2
Piping Spool Length (Mtrs)	2
Volume(Ltrs)	2.28
GPS PO No / Work Order No	Shibili Numan-Eurotech International LLC / Mail Reference

This is to certify that **Eurotherm PPR PN25 Pipe 63mm Pipe Spool / Female Thread Adapter 63mm X of 2 pcs (fitted in both pipe ends)** **Piping Spool**
 Was successfully hydrotested by **GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC** Representative

HYDROTEST PARAMETER'S

LOCATION OF TEST	MISFAH GPS YARD					
TEST MEDIUM	WATER					
AIR CONTENT % OF PIPELINE @ 50% OF TP	N/A					
VISUAL INSPECTION @ 100% OF TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.5	FINAL PRESSURE	37.4
STRENGTH TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.4	FINAL PRESSURE	37.4
LEAK TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	MAX PRESSURE	37.4	MIN PRESSURE	37.4
ACTUAL CHANGE IN TEMPERATURE AT TEST PRESSURE (DEG C)					N/A	°C
ALLOWABLE CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
ACTUAL CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
DURATION OF PRESSURISATION	1 Hour 55 Mins	FROM: 28th June, 2024	16:00	TO: 28th June, 2024	18:20	
DURATION OF STRENGTH TEST	1 Hour	FROM: 28th June, 2024	18:20	TO: 28th June, 2024	19:30	
DURATION OF LEAK TEST	1 Hours	FROM: 28th June, 2024	18:20	TO: 28th June, 2024	19:30	

INSTRUMENT'S DETAILS

INSTRUMENT DESCRIPTION	INS SERIAL NO	RANGE	CALIBRATION DATE	CALIBRATION DUE DATE
PRESSURE RECORDER	11260072004	0-60 Bar	1st Dec, 2023	30th Nov, 2024
PRESSURE GAUGE	9000R81P	0-60 Bar	9th June, 2024	8th June, 2025
DIGITAL PRESSURE GAUGE	707496	0-700 Bar	15th June, 2024	14th June, 2025
PRESSURE SAFETY VALVE	1064356	41 Bar	9th June, 2024	8th June, 2025

Comments:
 Eurotherm PPR PN25 Pipe 63mm Pipe Spool / Female Thread Adapter 63mm X of 2 pcs (fitted in both pipe ends)

Completed By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	PARTHIBAN	Signature: 	Date:	28th June, 2024
Designation	TESTING SUPERVISOR			

Approved By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	SENTHIL KUMAR	Signature: 	Date:	28th June, 2024
Designation	TESTING ENGINEER			



GPS Doc Reference No: GPS-FR-PS-OP-01

Page No: 1 OF 1



HYDROTEST COMPLETION CERTIFICATE



Project	1 & 1/2" 1 MTRS LENGTH HYDRO TESTING
Piping Detail	Eurotherm PPR PN25 Pipe 50mm Pipe Spool / Female Thread Adapter 50mm X1-1/2" of 2 pcs (fitted in both pipe ends)

Date	28th June, 2024	Piping Spool Size (inch)	1-1/2
Location	MISFAH YARD-OMAN	Piping Spool Length (Mtrs)	2
Hydro Test Pressure (Bar)	37.5	Volume(Ltrs)	1.98
Client/Contractor	EUROTHERM	GPS PO No / Work Order No	Shibili Numan-Eurotech International LLC / Mail Reference
Test Pack Number	02		

This is to certify that

Eurotherm PPR PN25 Pipe 50mm Pipe Spool / Female Thread Adapter 50mm X1-1/2" of 2 pcs (fitted in both pipe ends)

Piping Spool

Was successfully hydrotested by **GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC** Representative

HYDROTEST PARAMETER'S

LOCATION OF TEST	MISFAH GPS YARD					
TEST MEDIUM	WATER					
AIR CONTENT % OF PIPELINE @ 50% OF TP	N/A					
VISUAL INSPECTION @ 100% OF TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.7	FINAL PRESSURE	37.6
STRENGTH TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	INITIAL PRESSURE	37.6	FINAL PRESSURE	37.6
LEAK TEST PRESSURE(Barg)	37.5	NO LEAK FOUND	MAX PRESSURE	37.6	MIN PRESSURE	37.6
ACTUAL CHANGE IN TEMPERATURE AT TEST PRESSURE (DEG C)					N/A	°C
ALLOWABLE CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
ACTUAL CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
DURATION OF PRESSURISATION	1 Hour 5 Mins	FROM: 28th June, 2024	10:15 Hrs	TO: 28th June, 2024	11:05 Hrs	
DURATION OF STRENGTH TEST	1 Hour	FROM: 28th June, 2024	11:05 Hrs	TO: 28th June, 2024	12:05 Hrs	
DURATION OF LEAK TEST	1 Hours	FROM: 28th June, 2024	11:05 Hrs	TO: 28th June, 2024	12:05 Hrs	

INSTRUMENT'S DETAILS

INSTRUMENT DESCRIPTION	INS SERIAL NO	RANGE	CALIBRATION DATE	CALIBRATION DUE DATE
PRESSURE RECORDER	11260072004	0-60 Bar	1st Dec, 2023	30th Nov, 2024
ANALOUGE PRESSURE GAUGE	9000R81P	0-60 Bar	9th June, 2024	8th June, 2025
DIGITAL PRESSURE GAUGE	707496	0-700 Bar	15th June, 2024	14th June, 2025
PRESSURE SAFETY VALVE	1064356	41 Bar	9th June, 2024	8th June, 2025

Comments:

Eurotherm PPR PN25 Pipe 50mm Pipe Spool / Female Thread Adapter 50mm X1-1/2" of 2 pcs (fitted in both pipe ends)

Completed By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	PARTHIBAN	Signature: 	Date:	28th June, 2024
Designation	TESTING SUPERVISOR			

Approved By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	SENTHIL KUMAR	Signature: 	Date:	28th June, 2024
Designation	TESTING ENGINEER			



MODERN PROJECTS AL GHUBRA LLC

GPS Doc Reference No:

GPS-FR-PS-OP-01

Page No

1 OF 1



HYDROTEST COMPLETION CERTIFICATE



Project: 1/2" 1 MTRS LENGTH HYDRO TESTING

Piping Detail: EUROTHERM PPR PN 25MM PIPE SPOOL/ SOCKET / FEMALE THREAD ADAPTER 25mmX1/2"

Date	6th Sep, 2023
Location	MISFAH YARD-OMAN
Hydro Test Pressure (Bar)	35
Client/Contractor	Eutotech
Test Pack Number	01

Piping Spool Size (inch)	1/2
Piping Spool Length (Mtrs)	1
Volume(Ltrs)	0.12
GPS PO No / Work Order No	Arshad Ahamed-Eurotech International LLC / Mail Reference

This is to certify that

EUROTHERM PPR PN 25MM PIPE SPOOL/ SOCKET / FEMALE THREAD ADAPTER 25mmX1/2"

Piping Spool

Was successfully hydrotested by **GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC** Representative

HYDROTEST PARAMETER'S

LOCATION OF TEST	MISFAH GPS YARD					
TEST MEDIUM	WATER					
AIR CONTENT % OF PIPELINE @ 50% OF TP	-	N/A				
VISUAL INSPECTION @ 100% OF TEST PRESSURE(Barg)	35	NO LEAK FOUND	INITIAL PRESSURE	35.15	FINAL PRESSURE	35.1
STRENGTH TEST PRESSURE(Barg)	35	NO LEAK FOUND	INITIAL PRESSURE	35.1	FINAL PRESSURE	35.1
LEAK TEST PRESSURE(Barg)	35	NO LEAK FOUND	MAX PRESSURE	35.1	MIN PRESSURE	35
ACTUAL CHANGE IN TEMPERATURE AT TEST PRESSURE (DEG C)					N/A	°C
ALLOWABLE CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
ACTUAL CHANGE IN PRESSURE AT TEST PRESSURE					N/A	Barg
DURATION OF PRESSURISATION	45 Mins	FROM: 6th Sep, 2023 19:05 Hrs	TO: 6th Sep, 2023 19:50 Hrs			
DURATION OF STRENGTH TEST	1 Hour	FROM: 6th Sep, 2023 19:55 Hrs	TO: 6th Sep, 2023 20:55 Hrs			
DURATION OF LEAK TEST	1 Hours	FROM: 6th Sep, 2023 19:55 Hrs	TO: 6th Sep, 2023 20:55 Hrs			


INSTRUMENT'S DETAILS

INSTRUMENT DESCRIPTION	INS SERIAL NO	RANGE	CALIBRATION DATE	CALIBRATION DUE DATE
PRESSURE RECORDER	112737836002	0-40 Bar	3rd July, 2023	2nd July, 2024
PRESSURE GAUGE	9000R81P	0-40 Bar	9th July, 2023	8th July, 2024
PRESSURE SAFETY VALVE	1064356	41 Bar	9th July, 2023	8th July, 2024


Comments:

EUROTHERM PPR PN 25MM PIPE SPOOL/ SOCKET / FEMALE THREAD ADAPTER 25mmX1/2" - HYDRO TESTING COMPLETED SUCCESSFULLY AT A PRESSURE OF 35 BARG

Completed By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	SARAVANAN	Signature: 	Date:	6th Sep, 2023
Designation:	TESTING SUPERVISOR			

Approved By: GLOBAL PIPELINES SERVICES / MODERN PROJECTS AL GHUBRA LLC

Name:	VARUN KUMAR	Signature: 	Date:	6th Sep, 2023
Designation:	TESTING ENGINEER			



GPS Doc Reference No:

GPS-FR-PS-OP-01

Page No

1 OF 1

$\frac{1}{2}$ " EURO THERM PPR PN 25MM PIPE SPOOL /
 SOCKET / FEMALE THREAD ADAPTER.
 HYDRO TEST PRESSURE - 35 Bar
 Holding time - 1 Hour

ON 01:05 P M
 REMARKS BUKC-2128
 OFF 21:05 P M
 LOCATION
 DISC NO. 6th Sep, 2023
 METER NO.

